




BRIDGE

ONE INDUSTRY. ONE NETWORK. ONE BRIDGE.

FLAGSHIP COMPLETION HANDOFF

Tori's **Phase 2** prototype, finished.

A source-grounded record of what changed, how the complete 39-minute feedback review now appears in the product, what Phase 2 deliverables are ready, and what Dillon still needs to drive.

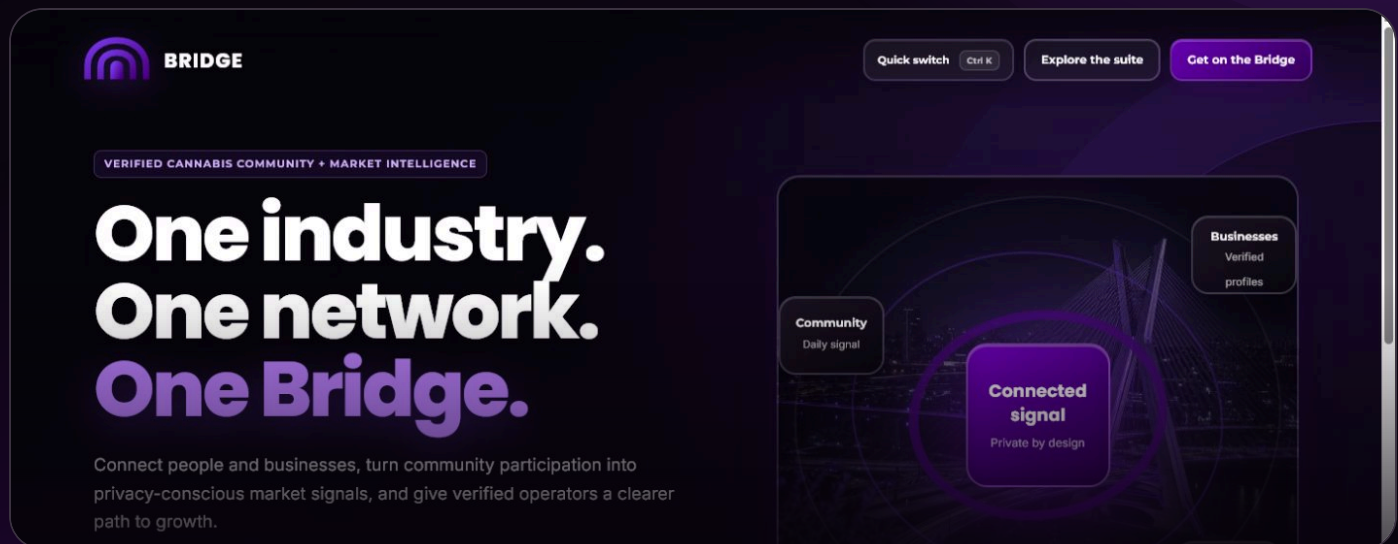

PREPARED

August 4, 2026

SOURCE BASIS

Tori review, July 23
Approx. 39 minutes

SLACK DESTINATION

#bridge-software-development
Attachment ready, not posted

The feedback is now a working product system.

This is no longer a loose visual prototype. The five primary spaces, their responsive behavior, key role boundaries, feedback-driven interactions, and Phase 2 implementation contracts now exist together as one reviewable package.

5

PRIMARY PRODUCT SPACES
COMPLETED

24

MATERIAL FEEDBACK THEMES
TRACED

5

PHASE 2 DEFINITION OUTPUTS
PACKAGED

0

DESKTOP OR MOBILE OVERFLOW
FAILURES

Home

Position + entry

Community News

Signal + feed

Create

Upload + target

My Profile

Identity + access

Explore

Find + favorite

What is complete


- Clear five-space information architecture and consistent navigation.
- Revised Home hierarchy with imagery, product entry, and useful market-signal framing.
- Responsive news-grid and classic-feed comparison.
- Promotion creation, real local asset selection, multi-audience targeting, and protected-detail guardrail.
- Public/B2B profile modes, responsible contacts, and recurring confirmation concept.
- Nationwide Explore filters, favorites, consumer utilities, and permissioned introductions.

What this does not pretend

- Illustrative records are not represented as live company, credential, or menu data.
- Client-side states are not represented as production security.
- Pricing, vendor visibility, providers, and final feed direction remain decisions.
- Authentication, storage, search, email, maps, ordering, and social links still need production integration.
- No deployment, Slack post, stakeholder approval, or public launch is implied.


Best-of-the-best standard applied: every important interaction has a visible state, sensitive information has an explicit boundary, mobile was designed rather than merely collapsed, and unresolved decisions remain clearly labeled instead of being buried inside visual polish.

The platform now reads as one connected product.

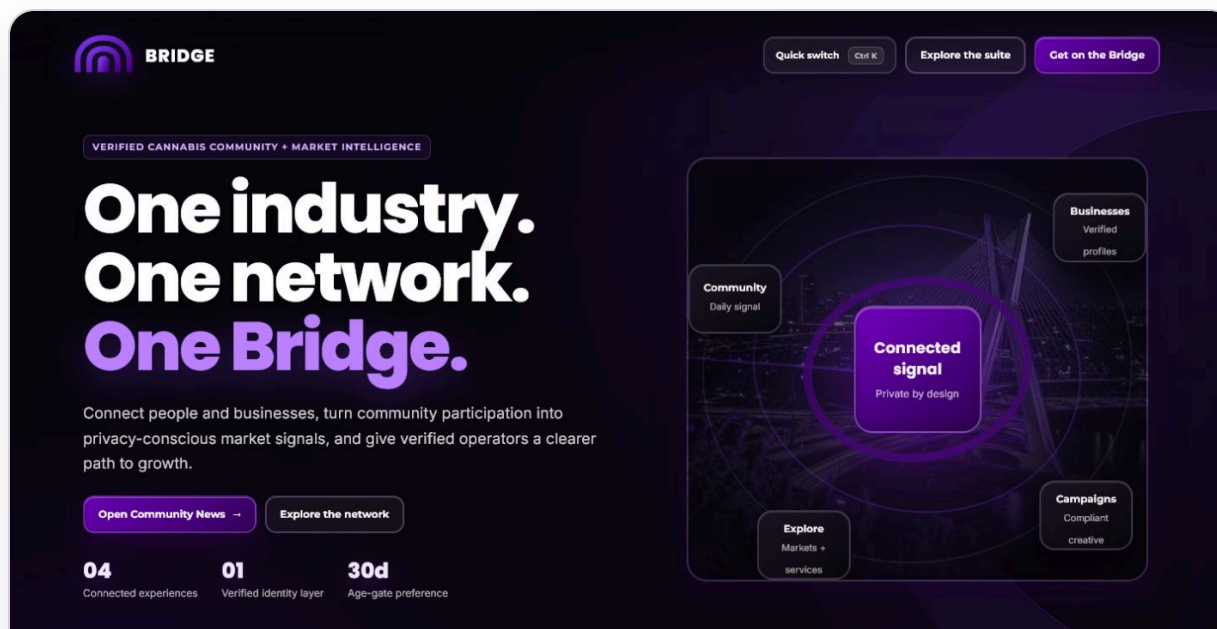


Home

Reduced hero dominance, clearer value, verified-network language, visual story strip, and direct entry to the four product spaces.

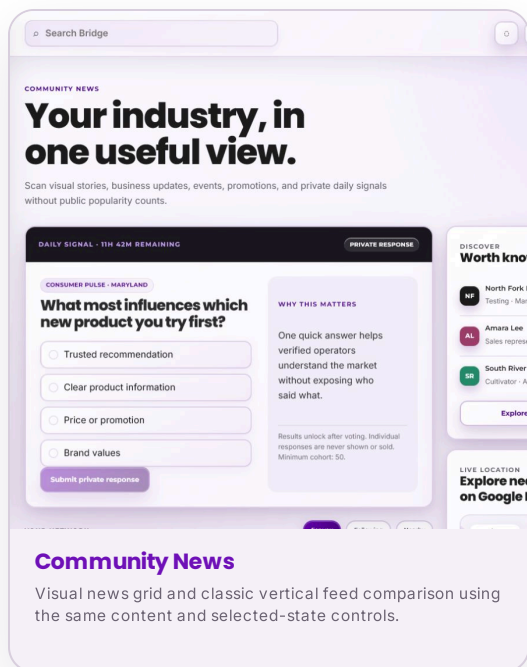

Community News



Visual news grid and classic vertical feed comparison using the same content and selected-state controls.

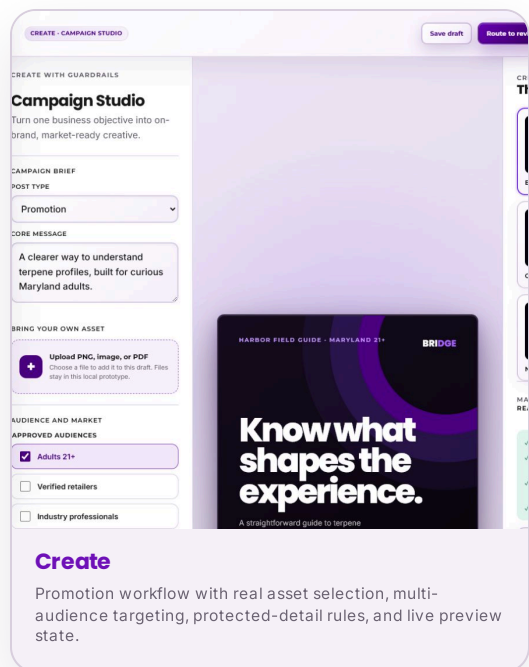

Create

Promotion workflow with real asset selection, multi-audience targeting, protected-detail rules, and live preview state.

Trust and discovery have real interaction depth.

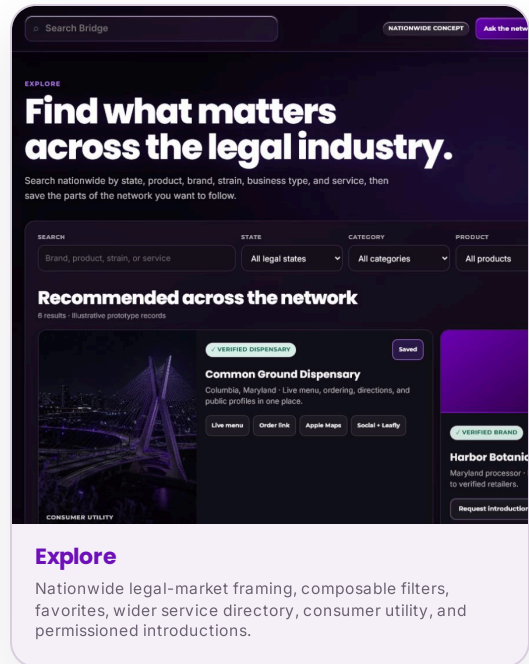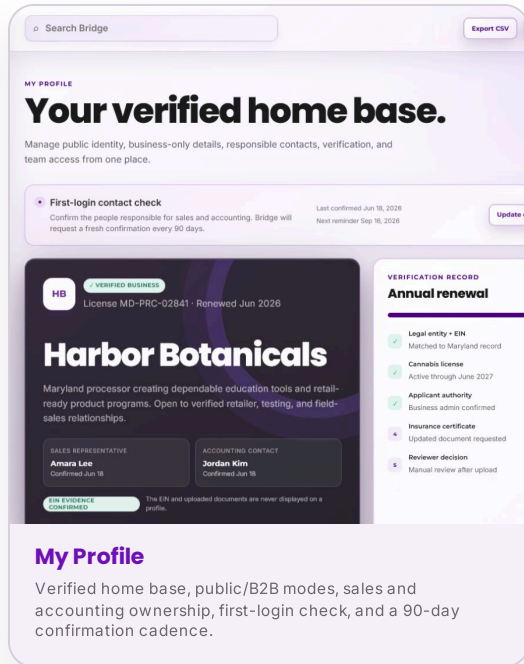

The result keeps the deep-purple Bridge character **Tori** responded to, while making the product easier to scan, easier to explain, and much more credible as a role-aware industry network.

Product-specific

Signal context, verified identity, legal-market discovery, audience protection, and responsible contacts are part of the experience rather than generic dashboard decoration.

Responsive

Desktop uses the product rail and wider editorial compositions. Mobile uses a persistent four-space dock and single-column decision flow.

Accessible states

Selected modes expose pressed state, uploads and counts announce changes, controls have labels, and reduced-motion behavior is preserved.

Screenshots are current local-browser captures from the completed static prototype on August 4, 2026. They are evidence of the interface package, not evidence of production integrations or a public deployment.

Tori's material feedback is traceable to a result.

FEEDBACK THEME	DISPOSITION	IMPLEMENTED RESULT OR CONTROLLED DECISION
Keep purple and dark Bridge character	IMPLEMENTED	Official dark-purple direction preserved and formalized in DESIGN.md.
More imagery, motion, and hover	IMPLEMENTED	Visual story strip, richer feed imagery, purposeful card motion, focus, and reduced-motion support.
Less giant hero type	IMPLEMENTED	Bounded desktop typography and earlier product utility.
Do not reject marketing metrics	IMPLEMENTED	Privacy-conscious, useful insight language replaces metrics-negative copy.
Clear routes and naming	IMPLEMENTED	Community News, Create, My Profile, Explore, and Home are consistent everywhere.
News grid versus vertical feed	APPROVE DEFAULT	Both responsive patterns are implemented with one-click comparison.
PNG/PDF/image upload and Promotion	IMPLEMENTED	PNG, JPEG, WebP, and PDF picker with size/type validation and preview feedback.
Multiple audiences and protected detail	PROTOTYPED	Multi-select audiences; protected content disables public targeting.
Sales/accounting contacts and recurring check	PROTOTYPED	Responsible contacts, first-login prompt, dates, confirmation state, and 90-day cadence.
Public/member/EIN-verified separation	POLICY LOCK	Public/B2B views and a field-level working matrix are ready for approval.
Vendor-to-vendor visibility	DECISION	Deny-by-default recommendation documented; Tori, Miraj, and legal must finalize.
Wider services directory	IMPLEMENTED	Bank, transport, lab, construction/HVAC/electrical, dispensary, and brand examples.
Nationwide filters and favorites	IMPLEMENTED	State, category, product, brand/strain/service search, result counts, favorites, and empty state.
Menu, order, Apple Maps, social, Leafly	PROTOTYPED	Consumer utility appears on a dispensary result; providers remain a production choice.
\$349-\$350 pricing	VALIDATE	Kept out of the UI and recorded as a hypothesis, not a final term.
Two-sided launch and major brands	BUSINESS WORK	Moved to launch readiness and network-density planning.
Do not rush	GOVERNED	Explicit stakeholder, data, technical, legal, test, and pilot exit gates.
HR idea	FUTURE ONLY	Excluded from Phase 2 MVP pending its own legal and privacy charter.

The repository contains the complete line-by-line checklist. This page condenses the major themes for Slack and stakeholder review.

All five definition outputs are now packaged.

01

Approved route and screen map candidate

The five spaces, labels, purpose, and handoff paths are reflected in the working prototype and product contract.

READY TO
REVIEW

02

Role, audience, and visibility matrix

Public adult, industry member, EIN-verified business, authorized staff, and admin capabilities are defined as the working baseline.

APPROVAL
NEEDED

03

Priority journeys and acceptance criteria

First-time discovery, feed comparison, targeted creation, profile confirmation, and nationwide discovery have testable outcomes.

COMPLETE

04

Responsive unresolved-choice prototypes

Homepage hierarchy, navigation, search, feed comparison, upload, audience rules, filters, favorites, and profile visibility exist in the same suite.

COMPLETE

05

Phased backlog and decision record

P0 lock, recommended vertical slice, network expansion, launch readiness, future HR, owners, dependencies, and exit gates are separated.

COMPLETE

Recommended production vertical slice

Targeted Promotion creation plus protected profile projection. This slice proves identity claims, uploads, audience rules, public/B2B field projection, contact confirmation, and auditability without requiring the entire nationwide marketplace first.

Product package

- PRODUCT.md
- DESIGN.md
- Phase 2 product contract
- Transcript implementation checklist
- Phased backlog and decision record

Engineering handoff package

- Identity and authorization claims
- Core entities
- Required API behaviors
- External integration decisions
- Server-enforcement and audit expectations

Phase 2 status: prototype and definition work are complete enough for a formal acceptance review. Phase 2 is not production-ready until the labeled policy and technical decisions are signed off.

Visibility is part of the product, not a hidden assumption.

CAPABILITY OR DATA	PUBLIC ADULT 21+	INDUSTRY MEMBER	VERIFIED BUSINESS	AUTHORIZED STAFF	ADMIN
Read public Community News	Yes	Yes	Yes	Yes	Yes
Participate in eligible signal	No	Yes	Yes	Yes	Yes
Create public promotion	No	Eligible creator	Yes	By permission	Yes
View public profile fields	Yes	Yes	Yes	Yes	Yes
View wholesale/relationship fields	No	Decision	Scoped	By permission	Audited
View sales/accounting contacts	No	No by default	Scoped	By permission	Audited
Confirm responsible contacts	No	No	Owner/admin	By permission	Audited
Request protected introduction	No	Eligible	Yes	By permission	Yes
View EIN/source documents	No	No	Status only	Status only	Verification staff only

What the prototype proves

- Public and verified views can be made legible to users.
- Protected audience rules can prevent an obvious targeting mistake.
- Contact responsibility and review cadence can live inside My Profile.
- Permissioned introduction can replace automatic contact exposure.

What production must enforce

- All protected projections and actions on the server.
- Verified claims, delegated staff permissions, and organization scope.
- Audits for protected reads, edits, verification, publishing, and introductions.
- Deny-by-default behavior when claims or relationships are uncertain.

Decision still required: the exact vendor-to-vendor field set and exceptions cannot be solved through design taste. Tori, Miraj, and legal need one field-level decision session before production work begins.

What still needs to come from me.

My next job is decision leadership, not more speculative screen production.

The prototype is strong enough to force the right conversations. I need to turn those conversations into recorded approvals, owners, and one production slice.

- 01 **Lead Tori's route-by-route acceptance review.** Capture accept, revise, or defer on every primary space.
- 02 **Lock the feed default.** Have Tori choose News grid or Classic feed while preserving the alternate as evidence.
- 03 **Convene the visibility session.** Bring Tori, Miraj, and legal together for fields, roles, vendor access, exceptions, and audit ownership.
- 04 **Select the vertical slice with Miraj.** Confirm scope, owner, API contract, fixtures, acceptance tests, and target date.
- 05 **Approve production imagery and copy.** Replace or approve any illustrative fixture before stakeholder or public use.
- 06 **Assign operations ownership.** Verification, moderation, reminders, introductions, support, and escalation each need a named owner.
- 07 **Split launch workstreams.** Pricing, major-brand recruitment, network density, and legal-state data are not interface subtasks.
- 08 **Protect the MVP boundary.** Keep HR out until its own legal, privacy, retention, access, and non-surveillance charter exists.

Decision artifact

One dated accept/revise/defer record after the Tori walkthrough.

Build artifact

One vertical-slice brief signed by Dillon and Miraj.

Ownership artifact

A named operational owner for every trust-critical workflow.

Minimum meeting outcome: approved route map, chosen feed default, visibility-session date, selected vertical slice, named imagery/copy owner, and next review date.

Additional Phase 2 work the product now entails.

Tori's review defines the experience. A responsible production path also needs the following foundations, even where the transcript did not specify implementation detail.

Identity, privacy, and authorization

- Verified server claims and delegated staff permissions.
- Field-level projection rules and audit events.
- Privacy notice, consent, retention, and data-access decisions.
- Legal review of advertising, state coverage, verification, and introductions.

Data and integration quality

- Authoritative legal-state and business sources with freshness rules.
- Upload storage, malware scanning, transformation, and PDF preview.
- Menu/order, maps, social, Leafly, and email provider choices.
- Explicit behavior for missing, stale, conflicting, or partial fields.

Operations and safety

- Verification queue, renewal, appeal, and escalation.
- Content moderation, reports, takedowns, and protected-content incidents.
- Contact-reminder ownership and introduction approval workflow.
- Support playbook, rollback path, and launch incident ownership.

Evidence and release quality

- Automated acceptance tests for every selected journey and role.
- Keyboard, screen-reader, contrast, reduced-motion, zoom, and mobile regression.
- Analytics definitions that separate delivery, activity, lead quality, and verified outcomes.
- Pilot success criteria and network-density thresholds before public expansion.

P0

Lock decisions

Tori acceptance, feed default, visibility matrix, vertical slice, and ownership.

NEXT

P1

Build the production slice

Authentication, uploads, audience rules, profile projection, contact event, and tests.

AFTER LOCK

P2

Expand the discovery network

Nationwide data, filters, favorites, provider utilities, introductions, and moderated feed.

FOLLOW-ON

P3

Prove launch readiness

Network density, operations, analytics, compliance, support, pilot, and rollback.

LAUNCH GATE

Reviewable evidence, clean boundaries, clear next move.

Structural package

Six route files, 18 required site files, and the Netlify function contract passed the repository verifier. ✓

JavaScript integrity

The completed app-v2.js parses successfully with Node syntax checking. ✓

Desktop route QA

Home, Community News, Create, My Profile, and Explore were inspected in the Codex in-app browser at 1440-pixel desktop width. ✓

Mobile route QA

All five primary routes were inspected at 390 by 844 with zero horizontal document overflow. ✓

Interaction proof

Feed switching, real local upload, protected audience behavior, profile confirmation/public mode, Explore filtering, and Favorites only were exercised. ✓

Deterministic design scan

Only incumbent local Bridge font families were warned; no change was made because they are intentional brand assets used with Poppins display hierarchy. ✓

Current completion boundary

- Prototype implementation: complete locally.
- Phase 2 product/design contracts: complete.
- Slack-ready PDF: complete.
- Stakeholder acceptance: pending review.
- Production integrations: pending decisions and engineering.
- Public deployment: not attempted because an exact existing Netlify site mapping was not verified in this package.
- Slack posting: not performed without delivery approval.

Recommended Slack message: **Tori's complete Phase 2 prototype pass is ready. The attached PDF shows what changed, how the feedback maps to the finished product, the decisions still needed, and the exact next actions I own.**

Next move: share this attachment in #bridge-software-development, schedule the acceptance review, and leave that review with six dated decisions rather than another open-ended round of feedback.

Source basis: the July 23, 2026 Tori review transcript summary, approved Bridge source package, current authoritative prototype repository, and the canonical Phase 2-and-beyond plan. Illustrative prototype records remain clearly separated from verified external facts.
